

# RRFHP Progress Update



# Power Intake and Head Race Tunnel




❖ Pre-commissioning of Spillway & Radial Gate No4 completed

❖ Electrical Control Room completed

❖ Total Removal of the Cofferdam ongoing

❖ Overall Progress 99%

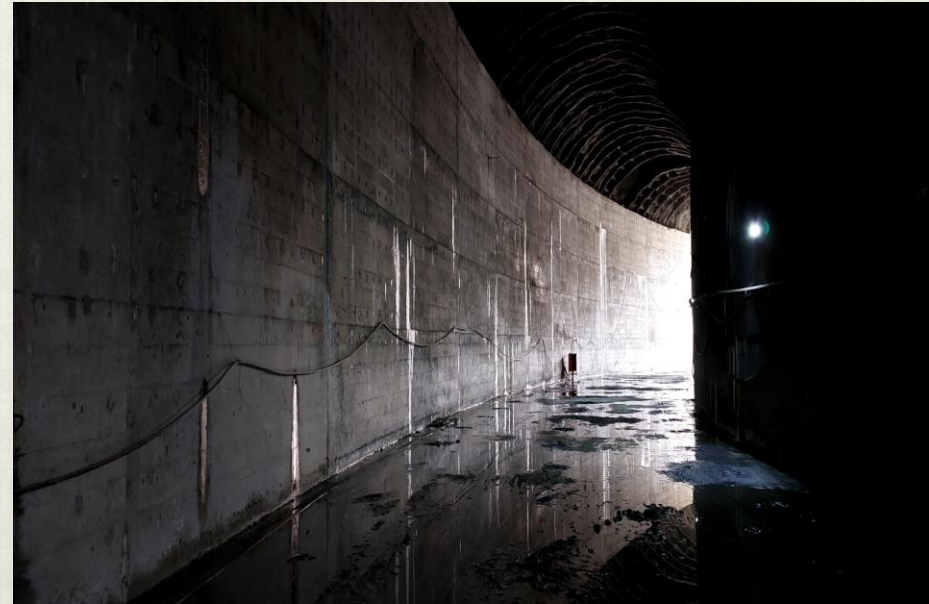

Head Race Tunnel: excavation complete, lining of walls and invert floor is complete, closing the adit to be completed by end of August 2022

# Power House Civil Works and Electromechanical Installations



1. Powerhouse building civil construction works completed; 2. Main Installation of Unit 1 completed; 3. Main Installation Unit 2 on-going; 4. Main Installation Unit 3 has started; 4. Installation of all auxiliary equipment.

# Switchyard 220 kV



- ❖ Installation of all equipment is complete
- ❖ Commissioning of individual equipment has started

# Overall Project Progress

- ❖ Total Power Plant Progress = 95%
- ❖ CP1: Hydro mechanical (Civil) works = 97%
- ❖ CP2: Electromechanical works = 92.5%

## Progress of Over-Head Transmission Lines Projects

### 1. Rwanda (Rusumo-Bugesera-Shango)

- ❖ Overall Progress: OHTL: 82%; Expected completion; October 2022

### 2. Burundi (Rusumo – Muyinga – Gitega)

- ❖ OHTL: 98.5%; Expected completion – August 2022

### 3. Tanzania (Rusumo – Nyakanazi)

- ❖ OHTL: 91%; to be completed by October 2022

# LADP I Projects

**Objective:-** To enhance regional economic and social development in the districts and communes in vicinity RRFHP area in Tanzania, Burundi and Rwanda. Projects include water supplies, dispensaries, schools and roads

**Rwanda:** All Projects implemented in Ngoma and Kirehe districts completed and are in operation

**Tanzania:** All Projects implemented in Ngara District completed except Rusumo Village water project whose construction is at 75% and is to be completed by October 2022

**Burundi:** All Projects implemented in Giteranyi and Busoni communes are complete and Projects Handing over is within August 2022

# LADP II Projects

- ❖ All Project proposals for Rwanda, Tanzania and Burundi have been submitted to the World Bank and undergoing approvals
- ❖ Preparation of procurement documentations i.e. bidding and tender documents is ongoing to save on time
- ❖ Commencement of LADP II Projects: November 2022

**THANKS**
